


9th St



G St (CONSTRUCTION LIMITS)


G - H Street (through Oct. 6)

- Ongoing open cut construction
- Tie-in work at G Street
- New manhole construction north of H St.

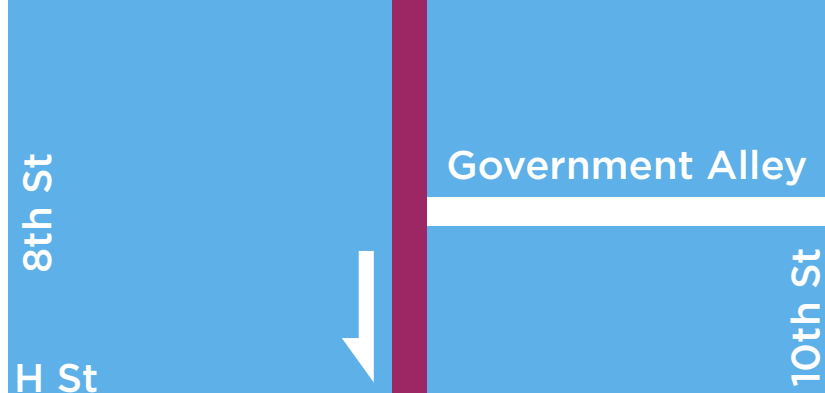

H - I Street (through Sept. 29)

- Clean up materials and equipment

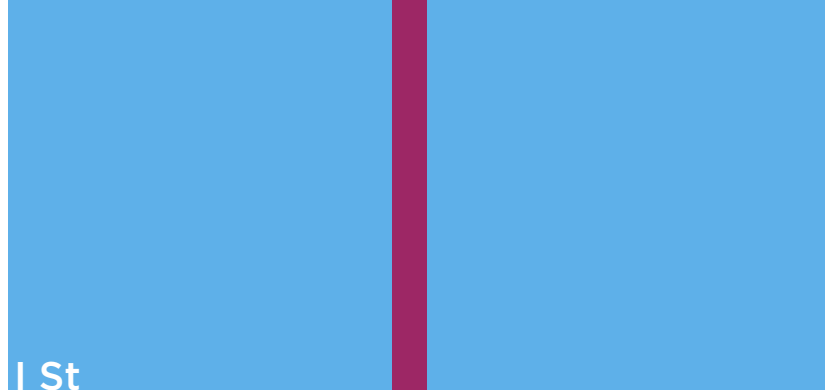


I - J Street (date to be determined)

- Replace landscaping at La Cosecha restaurant




J - K Street (through Oct. 6)

- Repair curb & gutter on east side of street
- Connect lateral pipeline to 60" pipeline
- Remove existing concrete and cobbles along west side of gutter near Rite Aid
- Replace ADA ramps at southwest corner of 9th & J (ongoing through Public Works)

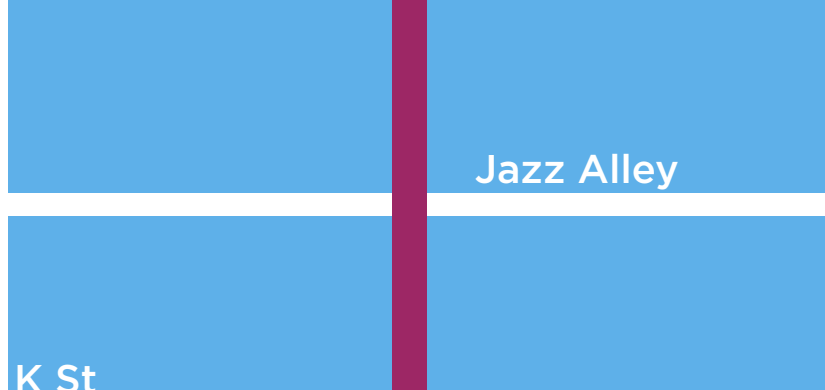


K - L Street (beginning Oct. 7)

- Final paving at Kayak Alley

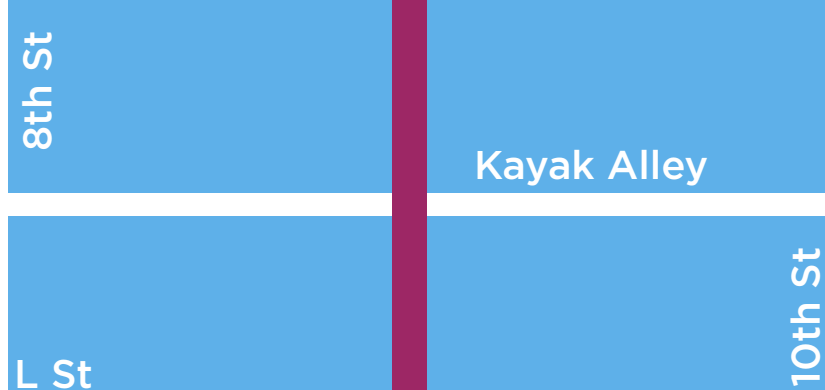


(CONSTRUCTION LIMITS)

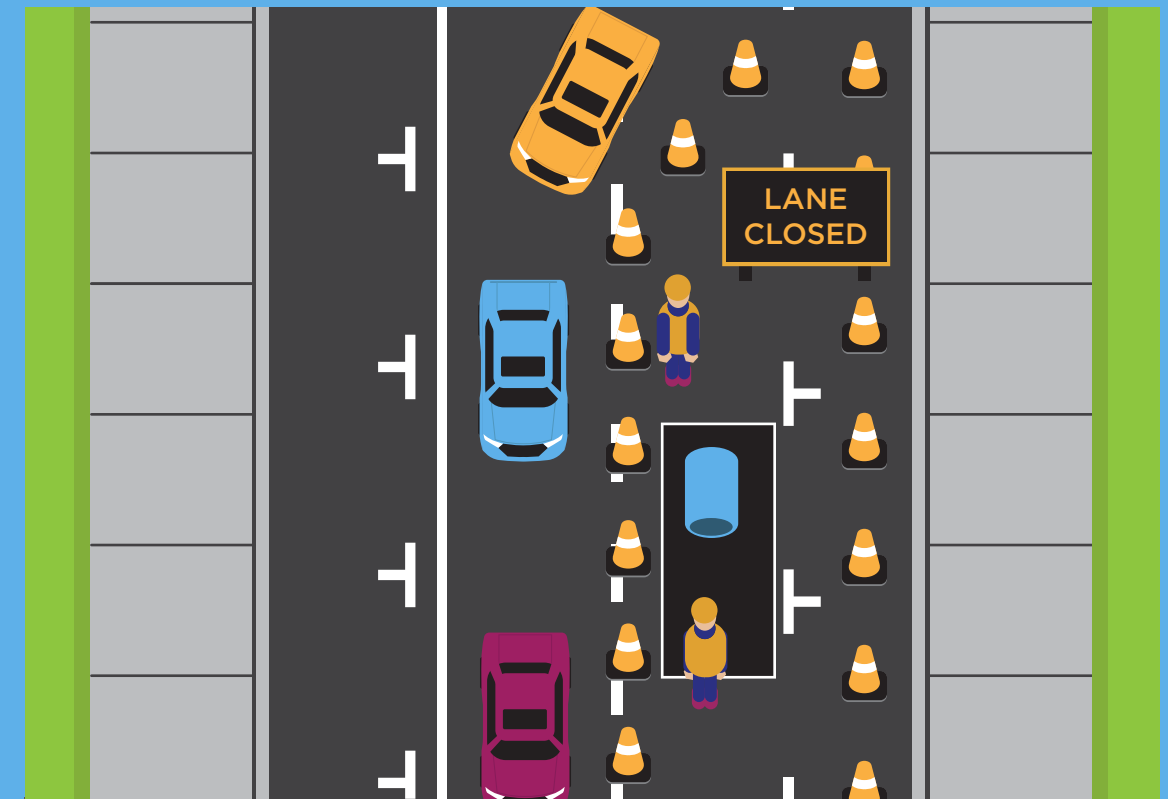

REMINDERS:

Temporary traffic control cones will be setup and taken down each day. Work hours remain 7 a.m. to 7 p.m.

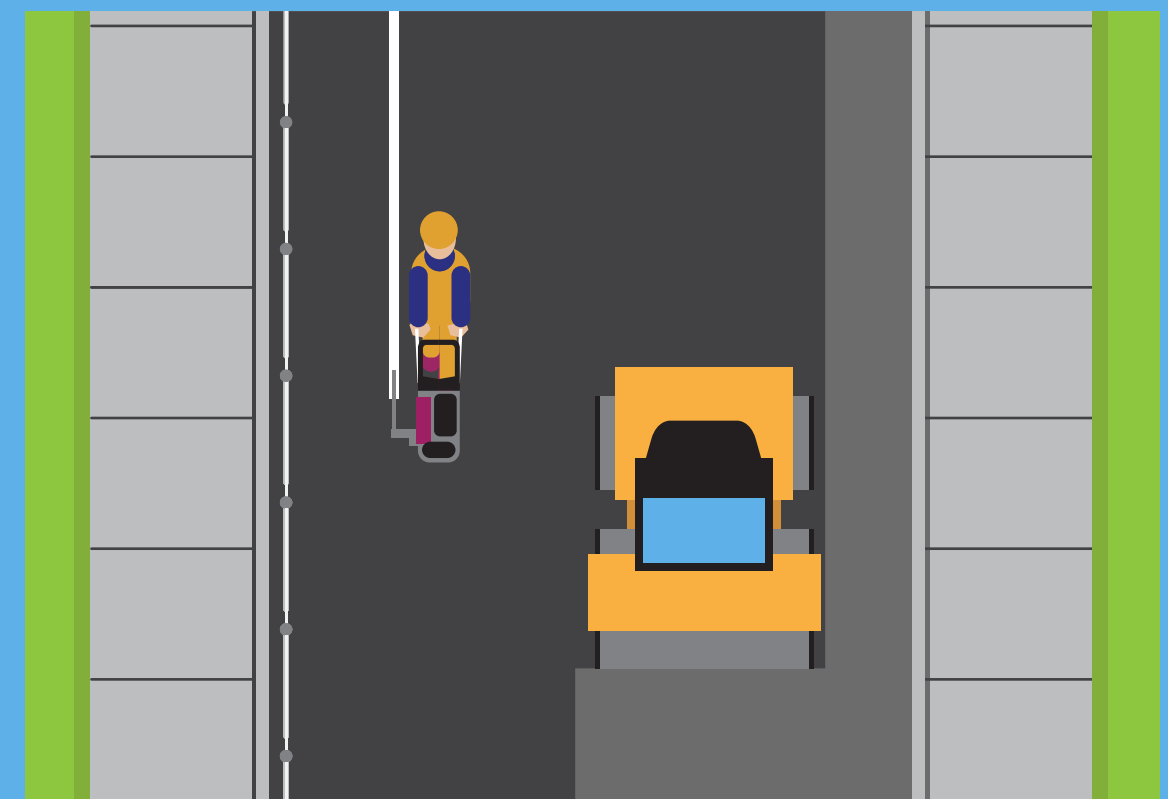

FINAL GRINDING, PAVING & STRIPING

Final grinding, paving, striping and bike lane painting for entire corridor is expected to begin in early October (starting at L Street and working north) and be complete by late October/early November.

Note: Work hours for grinding & paving activities will occur at night.
